

[previous](#) [Home](#) [next](#)

3.12.03 Gantt-Charts

This chart block includes the Gantt chart (bar chart) and the Gantt table, which is designed to complement the chart. A Gantt chart is a diagram to visualize the time planning of a project. The duration of a job or project is symbolized by the length of the bar in the timeline. The bars can be either actual data or target data. Events or milestones are represented as points in time. In Projectile processes are visualized in the project chart.


Here, the following charts can be generated:

- [Gantt-Chart](#)
- [Gantt-Table](#)

Gantt-Chart

The Gantt charts contain the time-related project charts in the system. The parameters available for the generated charts are various types of display types and the size of the generated jpg images. With display types, it can be selected whether bars should be generated above projects and jobs, whether milestones and networks should be displayed and whether the date for significant data should be generated.

In the Gantt chart, the planning data for the main project and the sub-projects (as described in chapter [2.5.03 Gantt-Chart](#)) is displayed as a gray bar with phases, milestones as gray diamonds, and the jobs as blue bars. The arrows between the jobs symbolize the order relationships. For this project, time and deadlines have been recorded. The recording for the projects and jobs are displayed as thin black bars and the estimates for the milestones as horizontal lines.

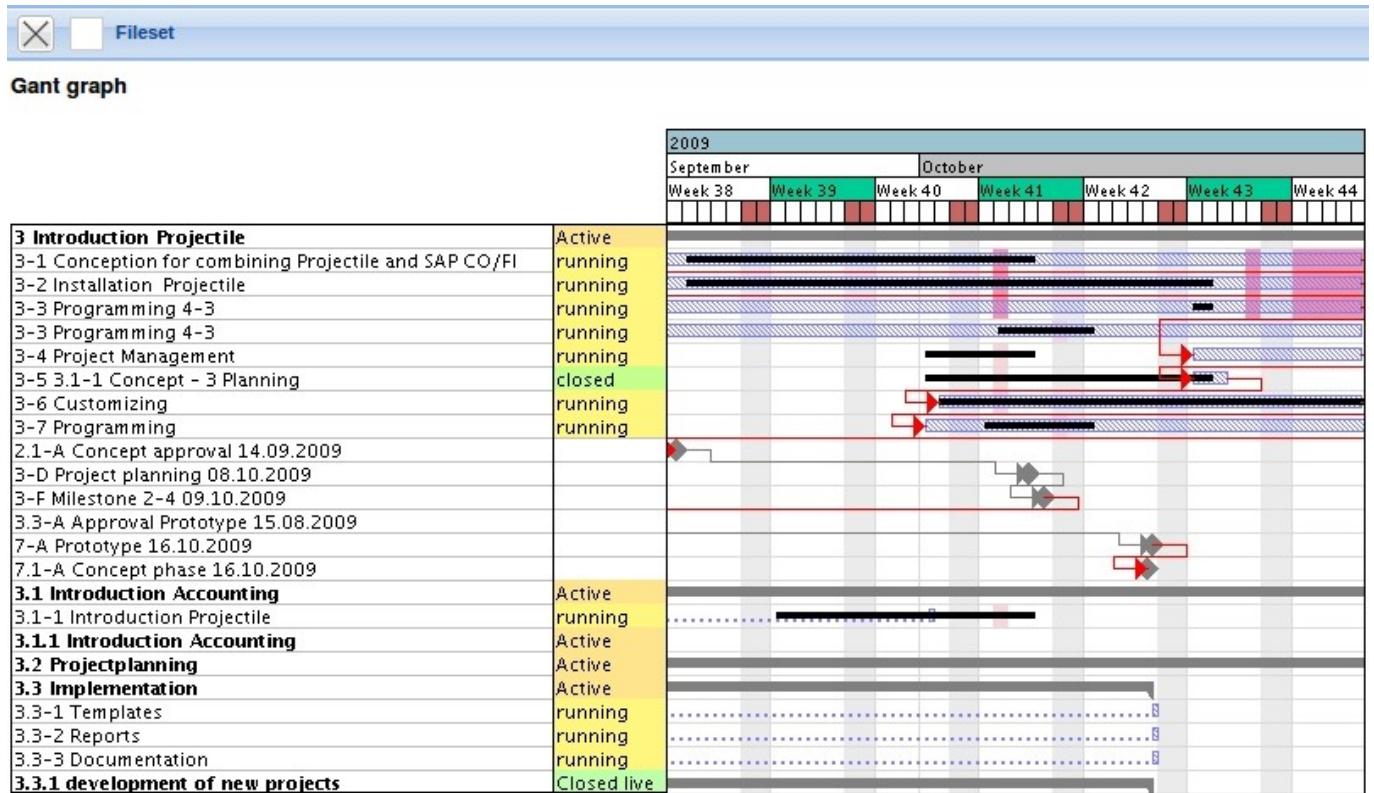

!!!!!!!!!!!! Interpretation des Beispiels: Das Projekt ist rechtzeitig gestartet und mit einem Arbeitstag (drei Kalendertage) Verzögerung abgeschlossen worden. Der erste Meilenstein ist rechtzeitig erreicht worden, die anderen Meilensteine haben sich geringfügig um einen Tag (EP.2-A) bzw. drei Tage (EP.3-A) verschoben. Die Unterprojekte Planung und Customizing sind rechtzeitig abgeschlossen worden und das Unterprojekt Einführung ist mit einem Tag Verspätung angefangen worden. Bis zum Projektende wird diese Verzögerungen auf drei Tage anwachsen.

Gantt-Table

This chart provides an overview of all the elements of the work breakdown structure and milestones of the selected projects. The plan time/effort, actual time/effort and the remaining time/effort of the elements, schedule and cost information as well as key figures are displayed as a list. The plan data is determined from the jobs and the actual times are extracted from the data entries of TimeTracker.

Projektauswertung												
Projekt	Mitarbeiter	Plan[h]	Ist-Zeit[h]	Differenz[h]	Rest[h]	Plan-Beginn	Plan-Ende	Ist-Ende	Status	Fertigstellung[%]	CPI	SPI
EP Implementation Projectile	1: Schaub Peter	260,00	250,00	10,00	0,00	09.02.2004	05.03.2004				1,04	1,00
EP-1 Projektleitung	1: Schaub Peter	36,00	37,00	-1,00	0,00	09.02.2004	05.03.2004	08.03.2004	erledigt, verspätet	100,00	0,97	1,00
EP.1 Planung	1: Schaub Peter	64,00	59,50	4,50	0,00	09.02.2004	17.02.2004				1,08	1,00
EP.1-A Konzeptabnahme 17.02.2004	1: Schaub Peter					17.02.2004	17.02.2004					
EP.1-1 Konzeptgespräche	1: Schaub Peter	24,00	20,00	4,00	0,00	09.02.2004	11.02.2004	11.02.2004	erledigt	100,00	1,20	1,00
EP.1-2 Pflichtenheft erstellen	1: Meier Dieter	40,00	39,50	0,50	0,00	11.02.2004	17.02.2004	17.02.2004	erledigt	100,00	1,01	1,00
EP.2 Customizing	1: Schaub Peter 2: Miller John	128,00	117,00	11,00	0,00	17.02.2004	02.03.2004				1,09	1,00
EP.2-A Prototyp 27.02.2004	1: Miller Frank					27.02.2004	27.02.2004					
EP.2-1 Entwicklung	1: Miller John	64,00	49,50	15,50	0,00	17.02.2004	26.02.2004	27.02.2004	erledigt, verspätet	100,00	1,32	1,00
EP.2-1 Entwicklung	1: Miller Frank	16,00	16,00	0,00	0,00	17.02.2004	26.02.2004	23.02.2004	erledigt	100,00	1,00	1,00
EP.2-1 Entwicklung	1: Schröder Sandra	16,00	15,00	1,00	0,00	17.02.2004	26.02.2004	20.02.2004	erledigt	100,00	1,07	1,00
EP.2-2 Dokumentation	1: Meier Dieter	24,00	26,00	-2,00	0,00	26.02.2004	01.03.2004	02.03.2004	erledigt, verspätet	100,00	0,92	1,00
EP.2-3 Testen	1: Schaub Peter	8,00	11,50	-3,50	0,00	26.02.2004	01.03.2004	01.03.2004	erledigt	100,00	0,70	1,00
EP.3 Einführung	1: Schaub Peter 2: Batzeck Klaus	32,00	36,50	-4,50	0,00	02.03.2004	05.03.2004				0,86	1,00
EP.3-A Systemabnahme 05.03.2004	1: Schaub Peter					05.03.2004	05.03.2004					
EP.3-1 Installation	1: Schaub Peter	8,00	8,00	0,00	0,00	02.03.2004	03.03.2004	03.03.2004	erledigt	100,00	1,00	1,00
EP.3-2 Schulung	1: Müller Julia	24,00	28,50	-4,50	0,00	03.03.2004	05.03.2004	08.03.2004	erledigt, verspätet	100,00	0,84	1,00

This chart supports more than 60 key figures. These key figures can be added in the [ReportDesigner](#).

↓ # Spalteninhalt (* Kennzahl)

<input type="checkbox"/> 1. Dokument
<input type="checkbox"/> 2. Gesamt_Plan[Pt]
<input type="checkbox"/> 3. Gliederungsstufe
<input checked="" type="checkbox"/> 3. Interne_Istkosten
<input type="checkbox"/> 4. Interne_Sollkosten
<input type="checkbox"/> 5. Interner_Gesamt-Planaufwand[Pt]
<input type="checkbox"/> 6. Interner_Gesamt-Planaufwand[h]
<input type="checkbox"/> 6. Interner_Istaufwand[Pt]
<input type="checkbox"/> 7. Interner_Istaufwand[h]
<input type="checkbox"/> 8. Interner_Planaufland[Pt]
<input type="checkbox"/> 9. Interner_Planaufland[h]
<input type="checkbox"/> 9. Interner_Stundensatz
<input type="checkbox"/> 10. Bis
<input type="checkbox"/> 11. Abschlußdatum_Arbeitspaket
<input type="checkbox"/> 12. Status_Arbeitspaket
<input type="checkbox"/> 13. Fertigstellung_aus_AP
<input type="checkbox"/> 14. CPI
<input type="checkbox"/> 15. SPI

From:
<https://infodesire.net/dokuwiki/> - **Projectile-Online-Handbuch**

Permanent link:
https://infodesire.net/dokuwiki/doku.php?id=en:handbuch:kapitel_3:3.12.03_gantt-diagramm&rev=1258022165

Last update: **2019/10/25 14:09**

