

[previous](#) [Home](#) [next](#)

3.12.03 Gantt-Charts

This chart block includes the Gantt chart (bar chart) and the Gantt table, which is designed to complement the chart. A Gantt chart is a diagram to visualize the time planning of a project. The duration of a job or project is symbolized by the length of the bar in the timeline. The bars can be either actual data or target data. Events or milestones are represented as points in time. In Projectile processes are visualized in the project chart.


Here, the following charts can be generated:

- [Gantt-Chart](#)
- [Gantt-Table](#)

Gantt-Chart

The Gantt charts contain the time-related project charts in the system. The parameters available for the generated charts are various types of display types and the size of the generated jpg images. With display types, it can be selected whether bars should be generated above projects and jobs, whether milestones and networks should be displayed and whether the date for significant data should be generated.

In the Gantt chart, the planning data for the main project and the sub-projects (as described in chapter [2.5.03 Gantt-Chart](#)) is displayed as a gray bar with phases, milestones as gray diamonds, and the jobs as blue bars. The arrows between the jobs symbolize the order relationships. For this project, time and deadlines have been recorded. The recording for the projects and jobs are displayed as thin black bars and the estimates for the milestones as horizontal lines.

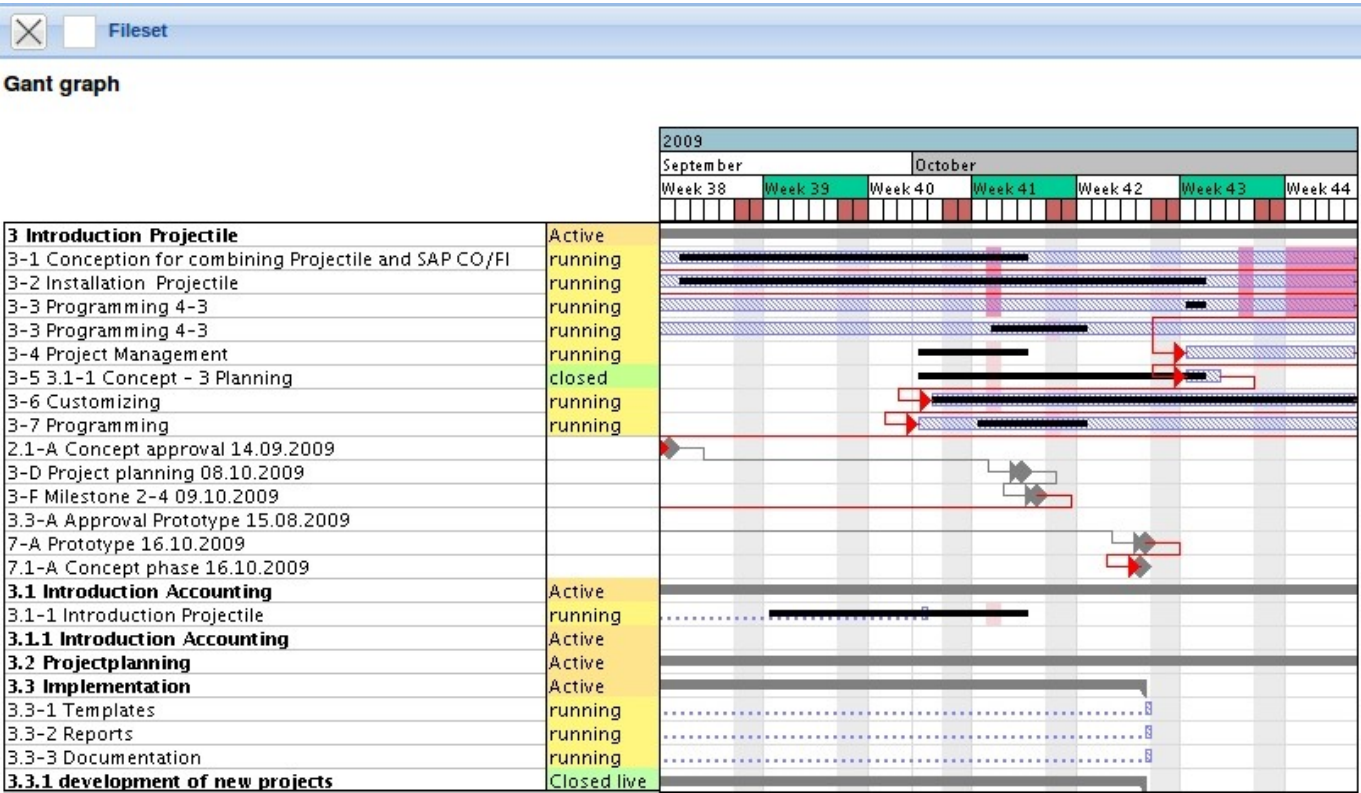

Fileset											
Gantt Table											
Projekt	Employee	EstimatedTimeH	ActualTimeH	DifferenceH	Rest[h]	Plan-Beginn	Plan-Ende	Ist-Ende	Status	Fertigstellung[%]	CPI SPI
3 Introduction Projectile	1: Conner Jane	41,30	134,67	-93,36	135,24	09.06.2009	31.12.2009				1,05 0,80
2.1-A Concept approval 14.09.2009	1: Hahn Katrina					14.09.2009	14.09.2009				
3-D Project planning 07.10.2009	1: Conner Jane					07.10.2009	07.10.2009				
3-F Milestone 2-4 30.10.2009	1: Hahn Katrina					30.10.2009	30.10.2009				
3.3-A Approval Prototype 15.08.2009	1: Jane Conner					15.08.2009	15.08.2009				
7.1-A Concept phase 16.10.2009	1: Conner Jane					16.10.2009	16.10.2009				
3-1 Concept for combining Projectile and SAP CO/FI	1: Jones Timothy	2,84	20,50	-17,66	33,03	09.06.2009	30.11.2009	23.11.2009	FINISHED	100,00	0,42 0,54
3-1 Concept for combining Projectile and SAP CO/FI	1: Conner Jane	1,42	0,00	1,42	8,00	09.06.2009	30.11.2009	23.11.2009	FINISHED	100,00	0,00 0,00
3-2 Installation Projectile	1: Jones Timothy	0,53	5,13	-4,60	0,00	09.06.2009	30.12.2009	23.11.2009	FINISHED	100,00	0,68 1,07
3-3 Programming 4-3	1: Jones Timothy	8,46	7,28	1,18	32,72	09.06.2009	30.10.2009	23.11.2009	FINISHED_LATE	100,00	1,00 0,18
3-3 Programming 4-3	1: Tate Adam	8,46	11,00	-2,54	29,00	09.06.2009	30.10.2009	23.11.2009	FINISHED_LATE	100,00	1,00 0,28
3-4 Project Management	1: Conner Jane	5,88	20,00	-14,12	16,00	19.10.2009	30.12.2009	23.11.2009	FINISHED	100,00	0,83 0,69
3-5 3.1-1 Concept - 3 Planning	1: Conner Jane	6,67	19,75	-13,08	0,00	19.10.2009	21.12.2009	20.10.2009	FINISHED	100,00	1,52 1,10
3-6 Customizing	1: Conner Jane	6,77	16,50	-9,73	3,50	02.10.2009	30.12.2009	23.11.2009	FINISHED	100,00	1,00 0,98
3-7 Programming	1: Tate Adam	0,00	31,00	-31,00	0,00	01.10.2009	11.12.2009	23.11.2009	FINISHED	100,00	0,00 0,00
3.1 Introduction Accounting	1: Hahn Katrina	0,00	3,50	-3,50	12,00	09.06.2009	30.11.2009				0,00 0,00
3.1-1 Introduction Projectile	1: Conner Jane	0,00	3,50	-3,50	12,00	09.06.2009	01.10.2009	23.11.2009	FINISHED_LATE	100,00	0,00 0,00
3.1.1 Introduction Accounting	1: Hahn Katrina	0,00	0,00	0,00	0,00	09.06.2009	22.07.2009				0,00 0,00
3.2 Projectplanning	1: Conner Jane	0,00	0,00	0,00	0,00	09.06.2009	30.11.2009				0,00 0,00
3.3 Implementation	1: Conner Jane	0,27	0,00	0,27	1,00	15.08.2009	16.10.2009				0,00 0,00
3.3-1 Templates	1: Jane Conner	0,27	0,00	0,27	1,00	15.08.2009	16.10.2009	13.11.2009	FINISHED_LATE	100,00	0,00 0,00
3.3-2 Reports	1: Jane Conner	0,00	0,00	0,00	0,00	15.08.2009	16.10.2009	13.11.2009	FINISHED_LATE	100,00	0,00 0,00
3.3-3 Documentation	1: Jane Conner	0,00	0,00	0,00	0,00	15.08.2009	16.10.2009	13.11.2009	FINISHED_LATE	100,00	0,00 0,00
3.3.1 development of new projects	1: Conner Jane	0,00	0,00	0,00	0,00	15.08.2009	16.10.2009				0,00 0,00
		82,87	272,83		283,49						

This chart supports more than 60 key figures. These key figures can be added in the [ReportDesigner](#).

#	Column content (* Figure)	
☐ 1.	Document	
☐ 2.		
☐ 3.	(Formula)	
☐ 4.	(Periods)	
☐ 5.	ActualBegin	
☐ 6.	ActualEnd	
☐ 7.	ActualTimeH	
☐ 8.	ActualTimePd	
☐ 9.	AssessableTimeH	
☐ 10.	AssessableTimePd	
☐ 11.	CompletionGrade	
☐ 12.	CompletionGradeJobBased	
☐ 13.	CompletionGradeSetInJob	
☐ 14.	CPI	
☐ 15.	Description	
☐ 16.	DifferenceH	
☐ 17.	DifferencePd	
☐ 18.	Document	
☐ 19.	Employee	
☐ 20.	EmployeeNames	
☐ 21.	EmployeeSalary	
☐ 22.		
☐ 23.		
☐ 24.		

From:
<https://infodesire.net/dokuwiki/> - **Projectile-Online-Handbuch**

Permanent link:
https://infodesire.net/dokuwiki/doku.php?id=en:handbuch:kapitel_3:3.12.03_gantt-diagramm&rev=1260811834



Last update: **2019/10/25 14:09**
