

[previous](#) [Home](#) [next](#)

3.12.08 Project Chart

The **project chart** implements the project-related charts. This includes the project overview chart, the [work breakdown structure](#) (project structure plan), target/actual comparison chart for projects and jobs, the [milestone-trend-analysis](#) chart, the visualization of [degree of completion](#), time sheets and a skill matrix.

The following charts can be generated here:

- [Project Overview Chart](#)
- [Project Structure Plan \(Work Breakdown Structure\)](#)
- [Project Chart Target/Actual](#)
- [Jobs Target/Actual](#)
- [Milestone-Trend-Analysis](#)
- [Degree of Completion Chart](#)
- [Skill-Matrix](#)

Project Overview Chart

This chart generates an overview of the most relevant key figures of the project. Here, the plan and actual time/effort and incurred costs/revenues are displayed as planned and actual values for the projects and sub-projects. Additionally in this chart, offer values and invoice values as well as degree of completion of projects and sub-projects are listed.


The planned costs specify the internal cost which are based on the planning data of the [jobs](#) and from the [budget administration](#). The internal costs are determined from tracking and recording ([TimeTracker](#)) and [cost recording](#). The project budget is, if necessary, defined in the project and the planned revenue is calculated from the external evaluation of the jobs and budget administration. The external revenue specifies all billable services in the system (time and costs).

Projektübersicht												
Projekt	Plan [h]	Ist[h]	Differenz Aufwand [h]	Plankosten [EUR]	Ist-Kosten [EUR]	Differenz Kosten [EUR]	Planumsatz [EUR]	Angebotsbetrag	Ist-Umsatz [EUR]	Differenz Umsatz [EUR]	Fertigstellung	
EP Implementation Projectile	36,00	37,00	-1,00	8.520,00	3.354,28	5.165,72	11.500,00	34.840,00	33.366,28	-21.866,28	100,00	
EP.1 Planung	64,00	59,50	4,50	3.080,00	2.782,50	297,50	6.400,00	0,00	0,00	6.400,00	100,00	
EP.2 Customizing	128,00	117,00	11,00	9.998,00	4.545,50	5.452,50	16.280,00	0,00	0,00	16.280,00	100,00	
EP.3 Einführung	32,00	36,50	-4,50	2.720,00	3.125,00	-405,00	3.040,00	0,00	0,00	3.040,00	100,00	
NAV Navision interface	8,00	22,00	-14,00	2.304,00	836,00	1.468,00	2.800,00	25.120,00	25.120,00	-22.320,00	60,00	
NAV.1 Planung	72,00	37,75	34,25	2.264,00	1.352,75	911,25	7.600,00	0,00	0,00	7.600,00	0,00	
NAV.2 Schnittstelle	76,00	52,00	24,00	4.480,00	3.640,00	840,00	6.800,00	0,00	0,00	6.800,00	0,00	
NAV.3 Basissystem	72,00	131,25	-59,25	3.800,00	5.547,50	-1.747,50	5.780,00	0,00	0,00	5.780,00	0,00	
	488,00	493,00	-5,00	37.166,00	25.183,53	11.982,47	60.180,00	59.960,00	58.486,28	1.693,72		

Project Structure Plan (Work Breakdown Structure)

The Work Breakdown Structure diagram illustrates the project structure. The [Work Breakdown](#)

Structure (project structure plan) in Projectile displays the relationship of the **project** and the sub-projects with the corresponding **jobs**. The logical structure of the project (project structure/project hierarchy) down to the jobs level is visualized graphically. This chart also contains important planned and actual data of the projects, sub-projects and jobs.

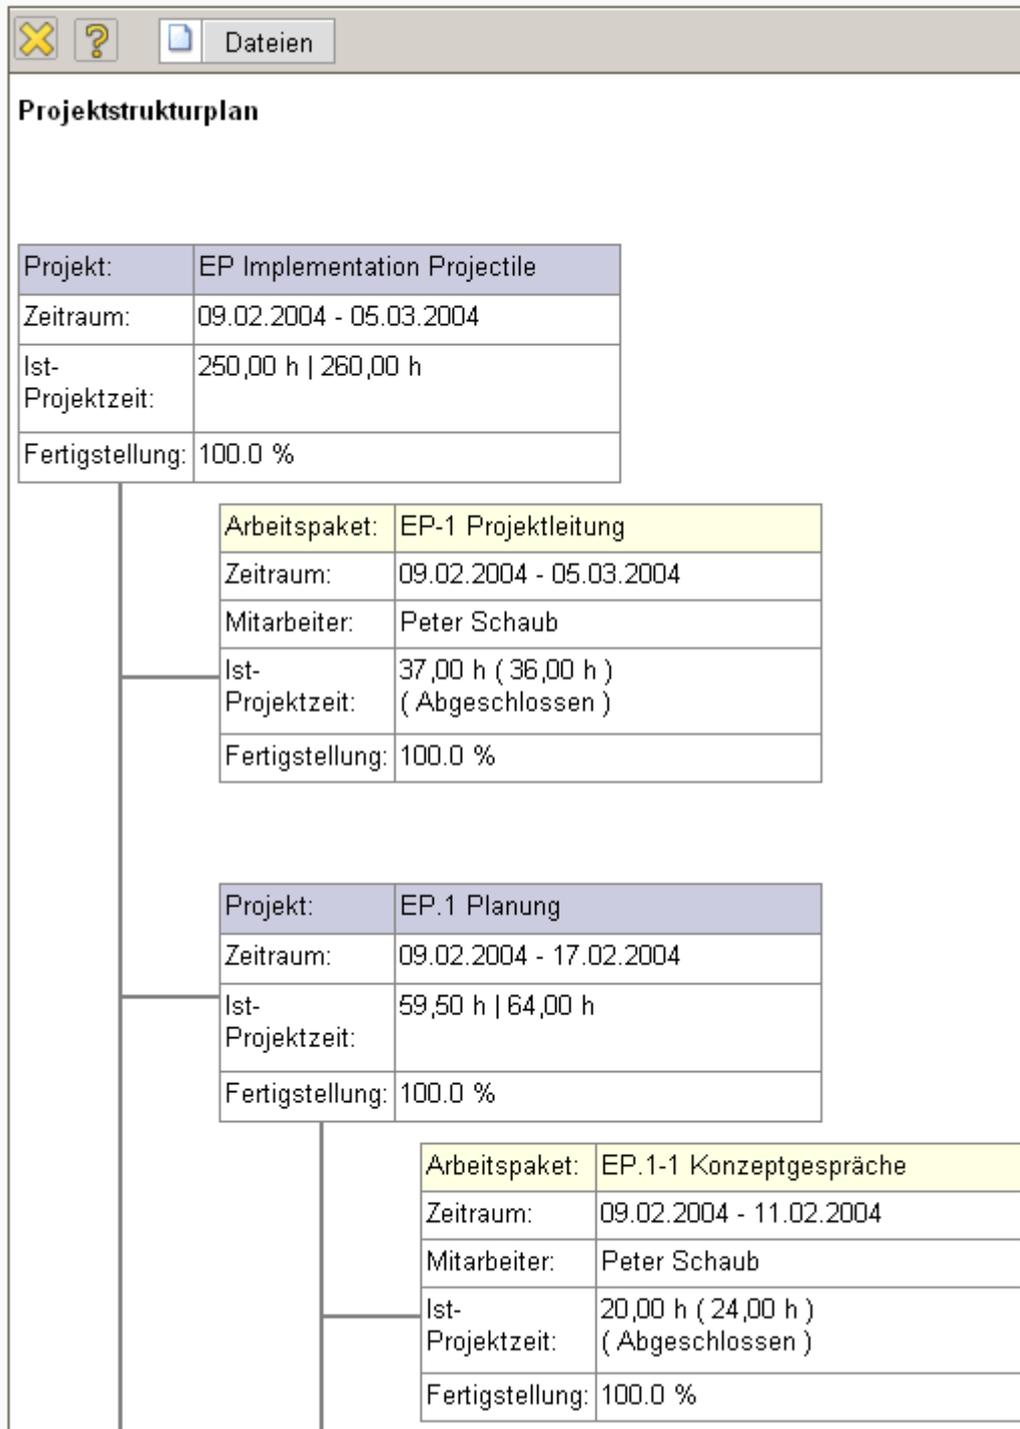


Project Chart Target/Actual

The project chart target/actual provides an overview of the work services of the individual **projects** including the corresponding sub-projects. The target times and actual times for the project are displayed as a diagram and as a list. The planning data is determined directly through the assignment

of the jobs to the project or sub-project and the actual times are used through tracking and recording in [TimeTracker](#).

The chart also contains information for planned-start and planned-end, of the project status and the estimated [degree of completion](#).

The chart can display the planned data and actual data graphically, if the option "with image" (format tab) is set.

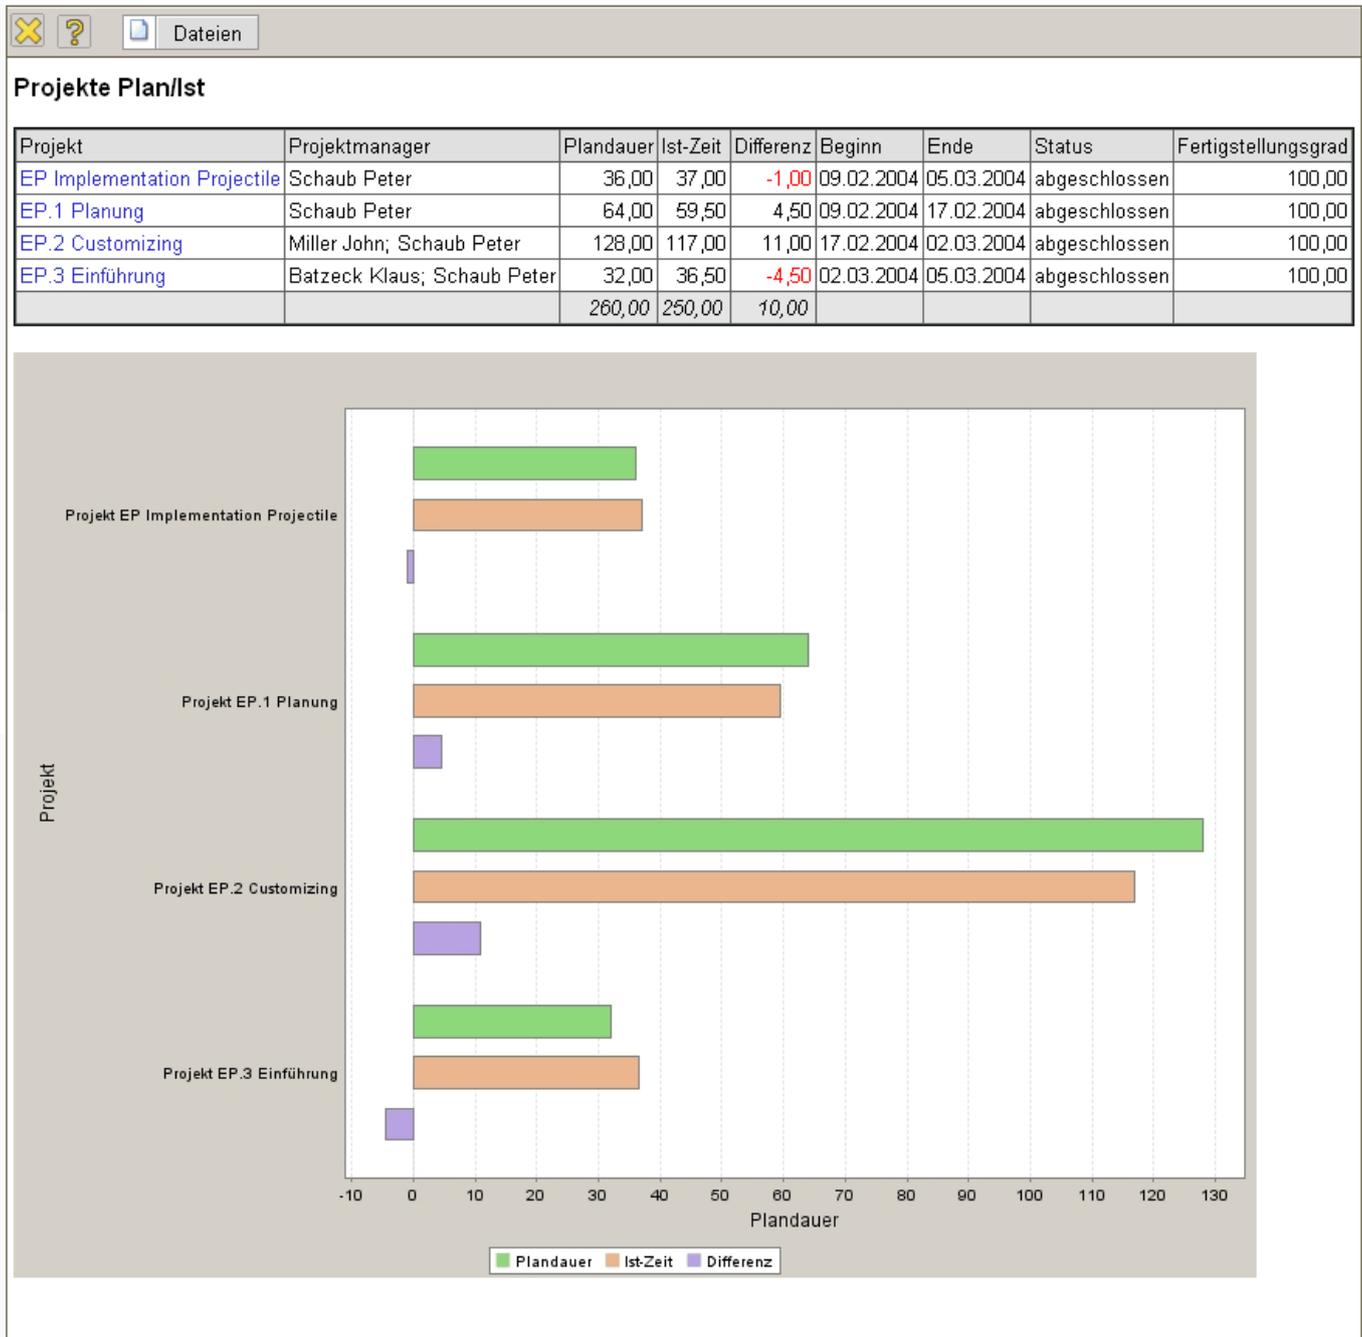

Jobs Target/Actual

The chart **jobs target/actual** provides an overview of the work services of the individual [jobs](#) of the selected projects. The planned times and actual times for the work packages are displayed as a diagram or as a list. The planning data is determined through jobs and the actual times are used

through tracking and recording in [TimeTracker](#).

The chart also contains information for planned-start and planned-end of the jobs, of the status (including the due date) of the jobs and the estimated [degree of completion](#) through TimeTracker.

Arbeitspakete Plan/Ist												
Projekt	Auftraggeber	Vorgang	Mitarbeiter	Plan [h]	Ist [h]	Rest [h]	Differenz	Plan-Beginn	Plan-Ende	Ist-Ende	Status	Fertigstellung [%]
EP.1 Planung	CONSULT GmbH	EP.1-2 Pflichtenheft erstellen	Meier Dieter	40,00	39,50	0,00	0,50	11.02.2004	17.02.2004	17.02.2004	erledigt	100
EP.2 Customizing	CONSULT GmbH	EP.2-2 Dokumentation	Meier Dieter	24,00	26,00	0,00	-2,00	26.02.2004	01.03.2004	02.03.2004	erledigt, verspätet	100
EP.2 Customizing	CONSULT GmbH	EP.2-1 Entwicklung	Miller John	96,00	79,50	0,00	16,50	17.02.2004	26.02.2004	27.02.2004	erledigt, verspätet	100
EP.3 Einführung	CONSULT GmbH	EP.3-2 Schulung	Müller Julia	24,00	28,50	0,00	-4,50	03.03.2004	05.03.2004	08.03.2004	erledigt, verspätet	100
EP Implementation Projectile	CONSULT GmbH	EP.1 Projektleitung	Schaub Peter	36,00	37,00	0,00	-1,00	09.02.2004	05.03.2004	08.03.2004	erledigt, verspätet	100
EP.1 Planung	CONSULT GmbH	EP.1-1 Konzeptgespräche	Schaub Peter	24,00	20,00	0,00	4,00	09.02.2004	11.02.2004	11.02.2004	erledigt	100
EP.2 Customizing	CONSULT GmbH	EP.2-3 Testen	Schaub Peter	8,00	11,50	0,00	-3,50	26.02.2004	01.03.2004	01.03.2004	erledigt	100
EP.3 Einführung	CONSULT GmbH	EP.3-1 Installation	Schaub Peter	8,00	8,00	0,00	0,00	02.03.2004	03.03.2004	03.03.2004	erledigt	100
				260,00	250,00	0,00	10,00					

The chart can display the planned data and actual data graphically, if the option “with image” (format tab) is set.


Milestone-Trend-Analysis

The Milestone-Trend-Analysis (MTA) chart displays trends for completing the defined [Milestones](#). The milestone-trend-analysis is a future-based instrument used for controlling deadlines of a [project](#): On regular reporting dates, the project [scheduling](#) is estimated through a query of trend data for the probable time of achieving the objective.

Die Auswertung Meilenstein-Trend-Analyse zeigt die Trends für die Erreichung der definierten [Meilensteine](#) an. Die Meilenstein-Trend-Analyse ist ein zukunftsbezogenes Instrument für die Terminkontrolle eines [Projektes](#): An regelmäßigen Berichtszeitpunkten wird die [Terminplanung](#) des Projektes durch die Abfrage von Trenddaten der voraussichtlichen Zielerreichung neu geschätzt. Aus dem Kurvenverlauf läßt sich ein Trend über die Termintreue des Projektes ableiten. Die Trendtermine für die Meilensteine können im Dokumenttyp [Trendtermin](#) verwaltet werden.

Der Verlauf der Kurven dieser Analyse wird wie folgt interpretiert:

- steigender Kurvenverlauf bedeutet eine Verzögerung ⇒ Das Meilensteinziel wird/ist verspätet erreicht,
- Kurvenverlauf waagrecht bedeutet Termintreue ⇒ Das Meilensteinziel wird/ist rechtzeitig erreicht und
- fallender Kurvenverlauf bedeutet: Das Meilensteinziel wird/ist verfrüht erreicht.

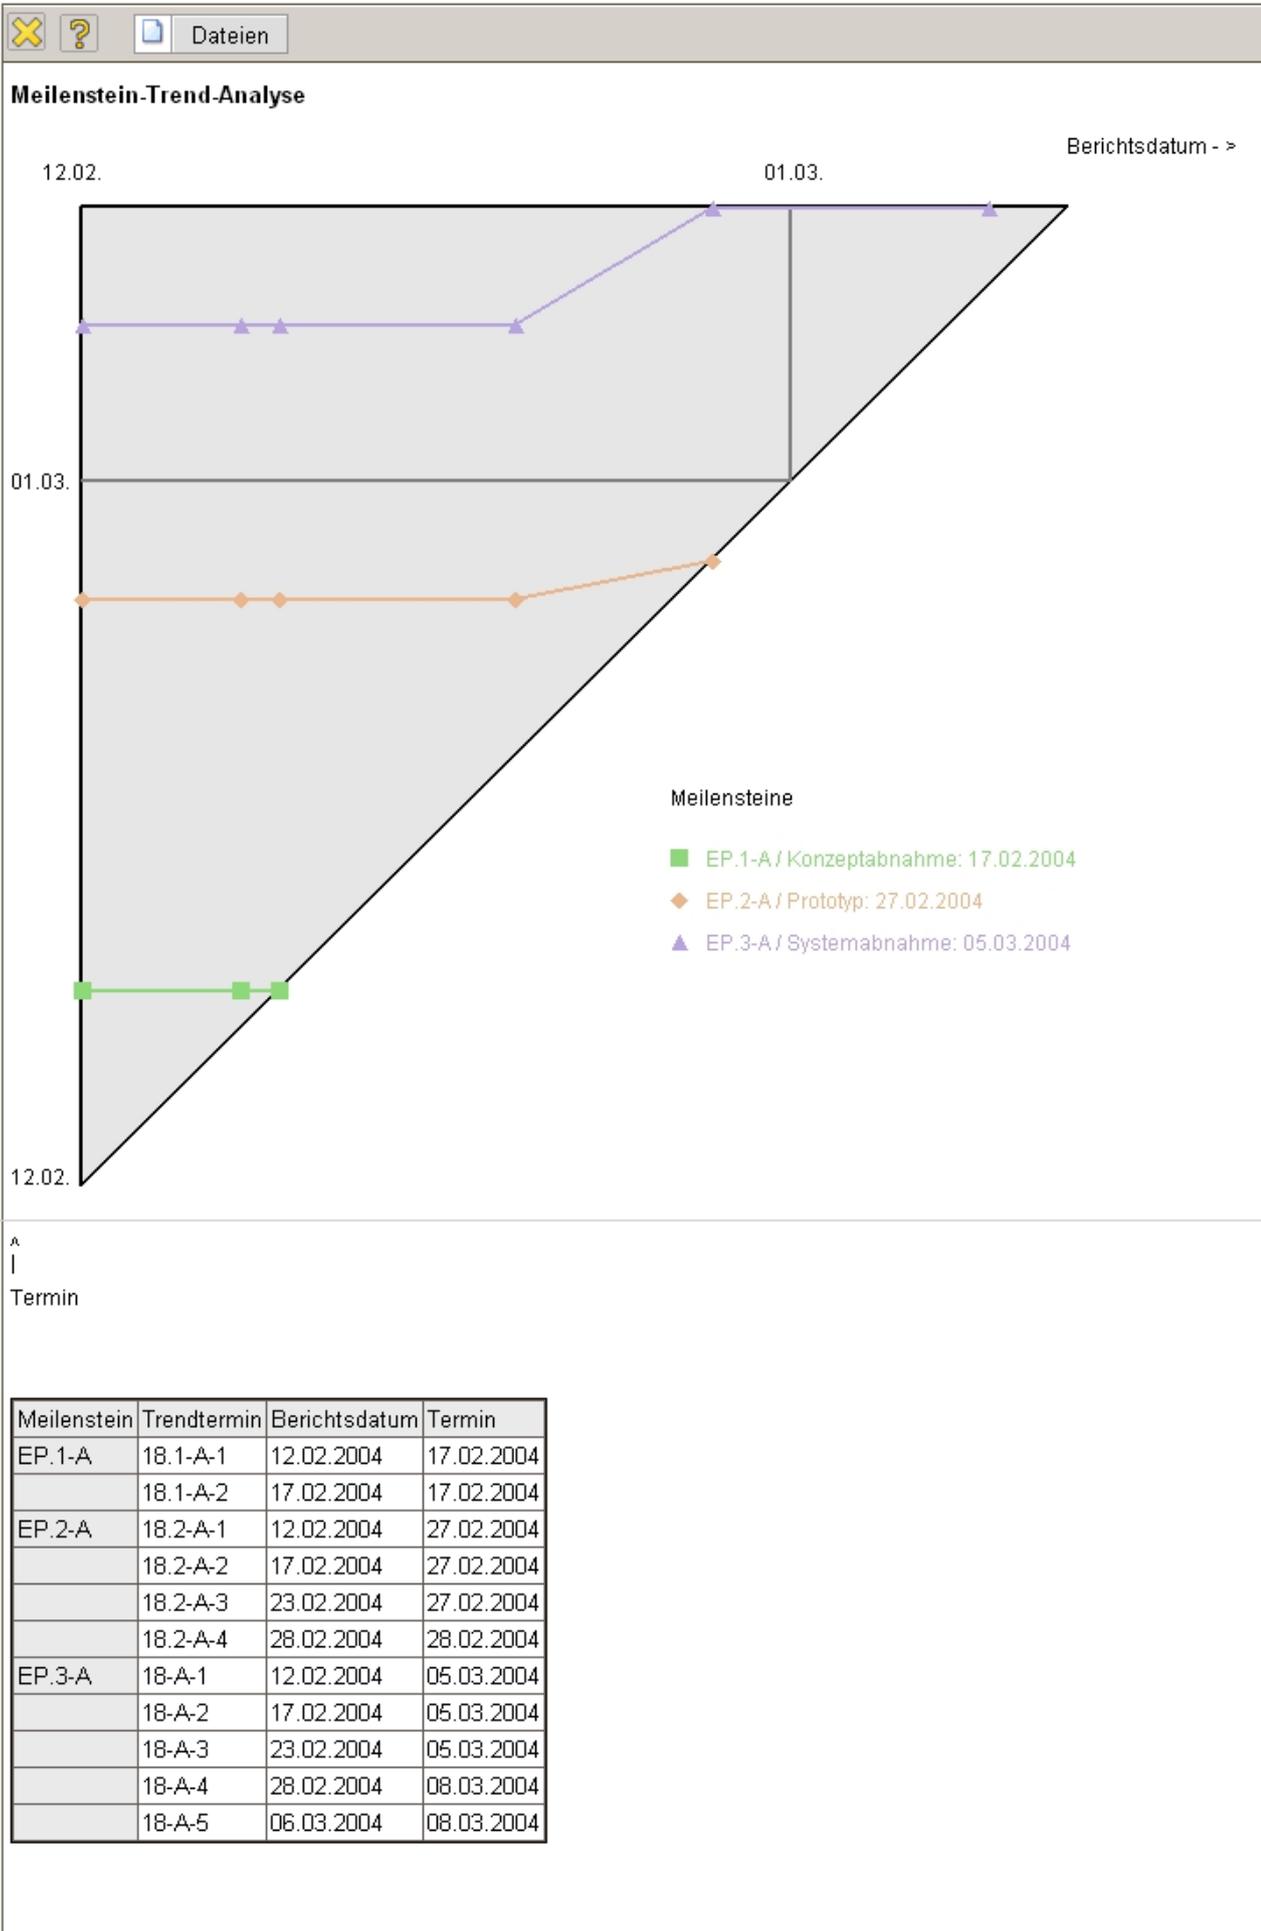


^
|
Termin

Meilenstein	Trendtermin	Berichtsdatum	Termin
EP.1-A	18.1-A-1	12.02.2004	17.02.2004
	18.1-A-2	17.02.2004	17.02.2004
EP.2-A	18.2-A-1	12.02.2004	27.02.2004
	18.2-A-2	17.02.2004	27.02.2004
	18.2-A-3	23.02.2004	27.02.2004
	18.2-A-4	28.02.2004	28.02.2004
EP.3-A	18-A-1	12.02.2004	05.03.2004
	18-A-2	17.02.2004	05.03.2004
	18-A-3	23.02.2004	05.03.2004
	18-A-4	28.02.2004	08.03.2004
	18-A-5	06.03.2004	08.03.2004

Fertigstellungsgrad

Die Auswertung Fertigstellungsgrad zeigt eine graphische Übersicht über die bisherigen Schätzungen für die Projekte und Arbeitspakete an. Diese Schätzungen können in den Projekten bzw. Unterprojekten oder im [TimeTracker](#) für die einzelnen Arbeitspakete vorgenommen werden. Weitere Informationen befinden sich im Abschnitt [4.2.7 Schätzungen](#).

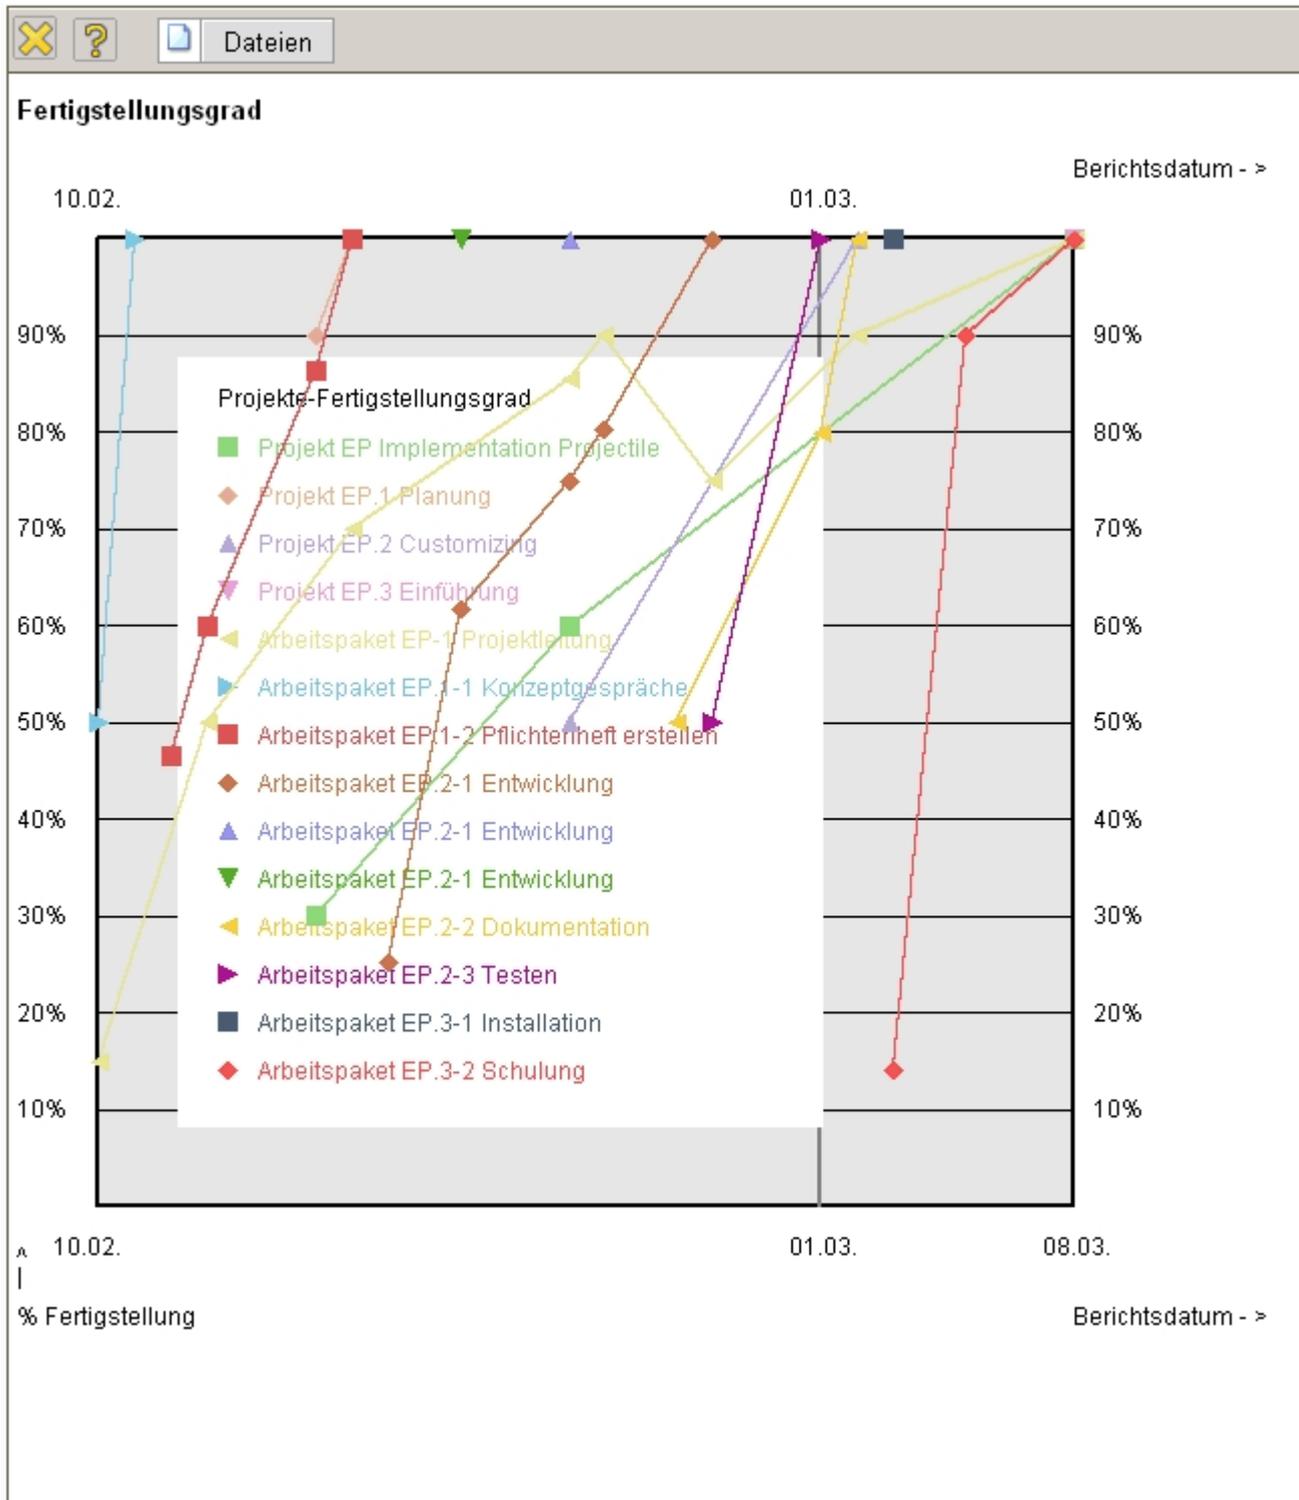

Skill-Matrix

Die Auswertung Skill-Matrix liefert eine Übersicht über die Projektleistungen für die selektierten Projekte und Unterprojekte in Bezug auf die einzelnen Tätigkeiten.

Topprojekt	Projekt	Programmierung - Java	Beratung	Testen	Analyse	Projektleitung	Installation & Einführung	Dokumentation, Handbücher und Leitfäden	Schulung/Workshops	Gesamt
EP Implementation Projectile		0,00	0,00	0,00	0,00	37,00	0,00	0,00	0,00	37,00
EP Implementation Projectile	EP.1 Planung	0,00	20,00	0,00	39,50	0,00	0,00	0,00	0,00	59,50
EP Implementation Projectile	EP.2 Customizing	79,50	0,00	11,50	0,00	0,00	0,00	26,00	0,00	117,00
EP Implementation Projectile	EP.3 Einführung	0,00	0,00	0,00	0,00	0,00	8,00	0,00	28,50	36,50
EP Implementation Projectile		79,50	20,00	11,50	39,50	37,00	8,00	26,00	28,50	250,00

From: <https://infodesire.net/dokuwiki/> - **Projectile-Online-Handbuch**

Permanent link: https://infodesire.net/dokuwiki/doku.php?id=en:handbuch:kapitel_3:3.12.08_projektauswertung&rev=1258456807

Last update: **2019/10/25 14:09**

